

Ottery St Mary

W^o Henry Aldridge,
 1855 To John Digby, L s d

Oct 15 th	1 Mason, 1 Lab ^r 1 day		3	8
	2 Barrows mortar, 25 Laths,	}	1	10
Nov	100 Nails, 25 Slate			
10 th	1 Mason, 1 day, (whitewash)		2	8
	1 Barrow mortar, 2 B ^o White rotter	}	1	11
	1 bucket whitewash line, 1 st glue			
13 th	1 Mason, 6 H ^{rs}		1	7
	1 st peck cement, 1 st glue, 1 st glue		1	6 ¹ / ₂
			<hr/>	
			13	2 ¹ / ₂


1856
 March 15th Settled J Digby

Ottery St Mary

The Feoffees of the Colyton Chauby
 1858 To John Digby, L s d

Jan 4 th	Making glazing and fixing a window complete at W. H. Aldridge	}	9	0
Apr 10 th	1 Mason 3 hours repairing walls of house 2 feet Lime & Board mortar to the glue		}	1
June 25 th & 26	1 Joiner 1 1/2 day repairing shutters at do 6 1/2 feet deal 12 x 1 1/2 Iron work & Screws 50 Clasp nails			4
	As per Agreement for Building a Derby complete at W. Aldridge		7	10 0
	Plastering & Refracting back wall of House		8	9 7
			<hr/>	
			12	0
			<hr/>	
			11	1 8

Settled
 October 18th 1858.
 John Digby Jun^r



Altary St Mary

Trustees of Colyton Charity

1854

To John Digby £ s d

As per agreement for painting windows front " 17 6

1855

July 30th

1 Mason, 1 Lab: 1/4 day, rising top of chimney, & putting up Chimney top - { " 4 7

Aug 5th

3 Barrows Brick Mortar, 40 Bricks " 3 2

2nd

1 Mason, 1 Lab: 1 day, pointing Roof " 3 8

3 Barrows Hair mortar " 1 9

4th

1 Mason, 1 Lab: 1/2 day, 1 Barrow Hair mortar " 2 5

12th

1 Mason, 1 Lab: 1/2 day, rep & deck at top " 1 10

2 Barrows mortar " 1 "

As per Agreement for putting up Chimney top " 5 4 "

As per Agreement for putting Stone in front of Pratts house " 10 0

£ 79 11

1856 Nov 16th
 John Digby



Altary St Mary Dec 1858

The Trustees of Colyton Charity

1858

To John Digby £ s d

As per Agreement for plastering and conpocasting the back wall of house occupied by W. A. Aldridge } 2 12 0

Oct 2nd

1 Mason 1/2 day repairing Roof, Linhey & at top } 1 4

12 Slate 12x6 2 Barrow Mortar 14 Bricks } 2 1

20

1 Mason 8 hours repairing Roof putting in gutter } 2 0

& at Aldridge } 2 0

12 Whimple Brick 2 Board Mortar 10 Slate } 1 4

£ 2 18 9

Altery St Mary

Trustees of Holy Trinity Church;

1856 To John Digby Esq

Nov: 17+22	1 Mason, 1 Lab: 4 days, Walling	" 14 8
	29 Barrows stone mortar, 4 Barrows Brick mortar, 200 Bricks, 4 Harveys	} 1 3 5
	5 Barrows hair mortar	
24+29	1 Mason 1 Lab: 2 1/2 days / Putting in drains, altering paving etc	} " 9 2
	30 Bricks, 2 Barrows mortar, 4 Barrows sand, 14 Syphon, 1 si Bend	
Decr 146	16 Junction, 3 si Pipes 4 Grates	} " 11 0
	1 Mason, 1 Lab: 3 days, Paving Rep ^d Roofs etc	
	6 Barrows sand, 7 Barrows mortar 40 Bricks, 10 Pav. Tile, 2 flat boards	} " 11 1
	6 Barrows stones	
4 th	1 Carpenter 1 boy 12 days, about Arch to gateway	} " 2 2
	11 ft Oak 4+3, 3 ft Sup: of 2" Oak 2 ft 6" of elm Board, Nails 6-	
		L 4 14 3

1856 The Feoffees of Colyton So J Sobry Esq
 Nov^r 8th Price for the Carriage of a Chimney top 0ⁿ 1ⁿ 0^c
 28th To 4 Sheaves of Iron Lab^r Materials
 To 12th behind chimneys Roof 0ⁿ 4ⁿ 6^c
 Dec^r 6th To 4 Bars of Iron for supports to
 Building Mrs Roots Chimney 0ⁿ 4ⁿ 0^c
 1857^r To 3 Joists Boarding Nails 0ⁿ 3ⁿ 6^c
 Feb^r 17th Lab^r to Kitchen Floor
 To a new Pair of Hinges & Fixing 0ⁿ 1ⁿ 0^c
 To a Door up Stairs 0ⁿ 1ⁿ 0^c
 1857 April 24th 0ⁿ 14ⁿ 0^c
 Settled J Sobry

1856 Mr Baker
 To Mr Flint
 for thatching Mrs prouts & S. D
 house 3 square feet at 2.6 d. 4. 6
 for spars 1st square - - - 0.3.0
 11 decr repairing thatch - 0.9.0
 for spars - - - 0.1.0
 0.13.0
 Settled Mr Flint

1856 The Feoffees of Colyton to Jas Bull
 To Work done at Cornhayne
 By Order of Mr Higgins 5 0
 Dec^r 24th To Redgin and Reparation for hay 1 0
 Settled Jas Bull

144
 OTTERY, Essex 1856
 Mr H. W. Oliver
 Bought of S. NORRINGTON,
 BUILDER, PLUMBER,
 Brazier, and Tin Plate Worker,
 WHOLESALE AND RETAIL IRONMONGER,
 BAR IRON, STEEL, AND WAREHOUSE. OILS & COLOURS.
 Agent to the Royal Exchange Assurance Fire and Life Office.
 Nov^r 6th To preparing Spring thatching } 5 0
 3rd 6th 1/4 and thatch } 4 6
 18 Apr 1857
 Paid Russell & Co

1836

The Colyton Freeffees due
to James Pullman for
Masons work done at
Mr. prouts to taking down chimney
Rebuilding the same and
Repairing and pointing the
wall against Mr. Boekes

17 to Masons and labour

one day .. 6 6

250 Brick Free due .. 8 9

4 bars of brick

Mortar for due .. 2 ..

18 do do .. 6 6

do do Mortar .. 2 ..

19 do do .. 6 6

2 bars of Mortar for .. 1 ..

20 Mason and labour

one day Mason

Half a day .. 3 3

4 bars of mortar .. 2 ..

21 Mason and labour

one day .. 4 ..

2 bars of mortar

Free due .. 1 ..

22 Mason and labour

one day and Mason

Half a day .. 3 3

2 bars of mortar for .. 1 ..

two flat tops Free chimneys 2 6

Cement on flat

for .. 7 6

£ 2 15 9

April 23

settled James Pullman



1853 Co Colyton Troffees to J. Pige
 Jan 5. 1 mason 1 lab = 3/4 Day to
 Rep^r the lin way roof 2 barrows of
 hair mortar 26 Slate - 5" 8.
 18. Mason 1/2 Day 4 tiles and
 mortar to shipe roof - 2 0
 Settled 7" 8

No. 401 to 407 HONITON UNION.
 PARISH OF HONITON,
 THE 26 DAY OF March 1853
 Received of Co Colyton Troffees
 the Sum of _____ Pound 17 Shilling and _____
 Pence, in respect of the Poor Rate of the above Parish, made the _____
 day of January 1853.

Rate made on £ 22. 15 Assessment,	£	s.	d.
at _____ in the Pound.		17	1
Arrear of former Rate - - - - -			
TOTAL -			

J. Pige
 ASSISTANT OVERSEER.

TAKE NOTICE—Unless the above Amount is paid on or before the _____ day of October
 instant, application will be made to the Magistrates.

Troffees to
 Mr Lang Co

Drawing Gravel	
Piles Stone 3 Days	9 a
Drawing Stone for gutter	
3 Days and half	7 b
1/2 hundred fence	3 a
Drawing & lorry turf	1 0
	<u>1 1 0</u>

Settled April 22nd 1853
 John Lang

1853.
 March 28. Received of Mr. Skinner on
 a Grant from the Troffees towards the
 Poor Rates the sum of Eighteen—
 Shillings—
£ 0. 18. 0 George Langford

1852		The Feoffees of Colyton Dr to J Dewey L. S. d		
Oct 30 th	3 1/2 Day	putting in plank in the Town Lake	0	1. 6
Nov ^r 16 th	1 Day	Reducing & Repairing Ladder	0	2. 0
Dec 27 th	1 Day	Cutting off Tree & at Cornells	0	2. 0
28 th 29 th 30 th	3 1/2 Day	preparing and putting in Stakes at ^{Green} Renspath	0	1. 6
1853 Jan ^r 6 th	1 Day	preparing Elm Stakes	0	2. 0
7 th	1/2 Day	do do do	-	1. 0
17 th 18 th	1 1/2 Day	putting in new Stakes in Mr. Hodges Orchard &	0	3. 0
25 th	1/2 Day	at the Market House	0	0. 6
Febr ^r 1 st	1 Day	fitting Gate & Post in Ty Lane	0	2. 0
March 6 th	1 Day	preparing Post & fitting Stakes in Mr. Buttons field	0	2. 0
7 th	1/2 Day	Cutting off & Hewing post	0	1. 0
31 st	1/2 Day	Repairing Shutters in Market House	0	1. 0
April 2 nd	1 Day	preparing Stakes	0	2. 0
4 th	1 Day	do do do	0	2. 0
6 th	1 Day	Repairing Railing at Cornells	0	2. 0
7 th	1 Day	do do do	0	2. 0
8 th	1 Day	do do do	0	2. 0
11 th	1 Day	Cutting down & firs at Lovelays	0	2. 0
12 th	1 Day	do do do	0	2. 0
13 th	1 Day	do do do	0	2. 0
26 th	1 Day	fitting Railing in Ty Lane Close	0	1. 0
			<u>£ 1. 19. 0</u>	
May 22 nd 1853 Settled John Dewey				

The Feoffes of Colyton
 1853 To Hy Adridge
 March 3 To Dressing
 Poultry as Per agreement
 F. C. C.
 Apr 21 pd
 Hy Adridge

1853 The Feoffes of the Chamber
 of Colyton
 To Jos. White
 To Whitewashing & Stopping 3
 Cottages in Colyford at 4s each 12.0
 Feb. 3 To 1 days work rep. Chimney 2.0
 do. Boy 1
 4 Self & Boy 1 day do. 2.7
 5 Self & Boy 1 day rep. Gutters 2.7
 25 Self & Boy 1 day rep. Pitching
 and Pivies 2.7
 Bucks 9^d Montan 1/9 2.6
 £14.10
 Settled March 4th 1853
 Joseph White

To: The Chamber of Colyton
 1852 To Wm Skinner
 April 25th 235 Copy Books 2 each 3 18 4
 April 29th 20 Cyphering Books, 6 each 14 "
 1853
 Feb 1st Printing Handbills for hitting Top Lane 5 "
 Close by Tender
 £4 17 4
 Paid to above Wm Skinner

1853 Colyton
 The Feoffees of
 To Sam Stocker
 Feb 19 Chimney top £ 15.0
 50 ft Shale & pipe 1. 9. 2
 repairing repairing
 & painting 20 ft of
 Old Shute Holdfast etc 0
 Suter Head for do 2. 6
 £ 2. 12. 8
 Settled April 29th 1853
 Sam Stocker

No. 401 to 406 HONITON UNION.
 PARISH OF HONITON,
 THE 23 DAY OF Nov 1852.
 Received of Mr. Colyton Feoffees
 the Sum of _____ Pound 15 Shilling and 4 1/2
 Pence, in respect of the Poor Rate of the above Parish, made the 26th
 day of October 1852.
 Rate made on £ 20.10 Assessment, } £ s. d.
 at 7/6 in the Pound. } 15 4 1/2
 Arrear of former Rate - - - - -
 TOTAL - 15 4 1/2
 Mace ASSISTANT OVERSEER.
 TAKE NOTICE—Unless the above Amount is paid on or before the 20th day of October
 instant, application will be made to the Magistrates.

Parish School Colyton March 25,
 1853
 Rec^d from Mr. Higgins on behalf of the
 Feoffees of Colyton the sum of eight
 Pounds and two shillings and six pence, being my salary
 due on the date hereof D. M. Stirling

This Receipt to be used by Agents only.
SUN FIRE OFFICE, LONDON.
 Pol. No. 1516001 Rec^d No. 31429
 RECEIVED of the Feoffees of Colyton the
 Sum stated in the Margin, for One Year's Premium and
 Duty on an Insurance of £ 510 in this Office,
 from Lady Day 1853 to Lady Day 1854
 the 5th Day of April 1853
 For the Managers of the Sun Fire Office,
 H. Stirling Agent.
 Insurances may be made for more Years than One, by a single Payment; and, in such cases, there will be a Discount allowed on the Premium
 and Duty, for every Year except the first.
 All persons insuring with this Office, are required to pay their Premium and Duty within fifteen days after the Quarter-day on which they are due,
 whether the usual Notice of the payment being due has been received by them or not. And in default of such payment the Policy will be void, and the
 Assured will be excluded from all benefit from it.
 Printed by HARRISON & SON, 45, St. Martin's Lane

1852		The Feoffees of Colyton Dr	
		to Jm Brown	
May 10	2	Oz Blank cards	6
		Account Books	10
	18	jar Ink	10
July 5	6 ^{ls}	Whiting 6	10 ^{1/2}
	16	10y Cork	3
	22	jar Ink	10
	27	3 Bottle Ink	3
	28	et ails	1 ^{1/2}
Aug 14	1 ^{ls}	Nails	3
	20	100 Clasp 3 Bottle Ink 4	13
		pr Hinges	4
		Norfolk Latch & Catch	4
	21	Door Lock 1/6 Staple 2	8
	23	Screws & Wire	3
Sep 30	1/2 ^{ls}	Compositas	4
Oct 4		jar Ink	10
	5	1 ^{ls} Nails	3
Nov 2	1 ^{ls}	do	3
Dec 15	2	Oz Plain Cards	3
	30	1 ^{ls} Sample Nails	3
Jan 17	1 ^{ls}	Nails	3
	25	jar Ink	10
Feb 8	1	Set do	14
Mar 7	1 ^{ls}	Nails	3
Apr 6	15 ^{ls}	do	39
	11	5 ^{ls} do	3
	13	1 ^{ls} do	3
			100

£ 100.
 Settled May 3rd
 Brown

1853 Thomsen Ammings bill per
 Mapens labor done in
 Redmoregreen for the
 Fodder and 20 Men by the
 Debt of Mr. Huggens - L. 1. 1. 0
 To Building of 80 Rope
 15 Feet of Flint wall
 Finding all Materials } L. 4. 6
 At 6 per Rope - - -
 To Pitching of the yard 6 feet
 At 5 per yard finding all } L. 11. 0
 Materials - - -
 Gates across the Road } L. 3. 9
 15 feet at 3 per foot
 L. 25. 19. 3. 4

Settled June 30th 1853
 J. H. Thomsen Ammings

1852

Harness Ammings for Mapors
Liber Don for the Footpces and

20 Men by the Order of Mr Higgins
(County) 23 Men 3 Partes of Day opening
Gutters in the Churchyard - 1 0.1.6

December 27 Self Day going to Loring
Bout Moterls for the green } 0.2.2

28 Self and Man 3 Partes of Day
Repairing Tilling on the School house 3.1.4

Moterls for Dy - 0.8

31 Self Day maring in the green 2.2

1853

January 4 Self half Day blowing pipes 1.8

12 Self Day opening pipes, 2.2

In the Churchyard

12 Self and Man 3 Partes of Day
Opening the Arch in } 3.1.4

Mr Rocketts docked

April 16 Self Day Repairing the tank } 2.2

In the Square

Moterls for Do - 0.9

20 Self and Man 3 Partes of Day
Cleaning out of all the tanks 3.1.4

£ 12.0

Bill as per Contract - 25-19-3

Settled Aprue 30th 1853 27-1-3

Witnessed Thomas Ammings

252 the Feoffees of Colyton
 Dr to J Lake £ 0 0
 March p^r Doors rep^d " 0 6
 April Square Staple Catch & Nail " 0 6
 Settler J Lake £ 1 0

February 26. 1853

Work done for the feoffes by John Moore
 At Cowshayme to offcutting Elm & 2.0

feet in	by	feet in	Line	
6-0	—	3-6	—	0 21-0
6-0	—	3-0	—	0 18-0
6-0	—	2-6	—	15-0
5-4	—	3-6	—	19-0
7-0	—	4-0	—	28-0
5-0	—	9-6	—	47-4
5-0	—	10-9	—	53-9
15-6	—	9-11	—	153 3
13-6	—	7-3	—	100-9
13-3	—	8-6	—	112-6
14-6	—	7-6	—	108-6
				35
		off cuts 7.		402-3

feet inches
 402-3 off sawing 3-6 per hundred — 1-4-6
 £ 1-4-6

Settled June 24th 1853
 John Moore ~~Settler~~

MARKET PLACE, COLYTON.

Colyton Feoffees

TO HENRY MATTHEWS,
BOOKSELLER, STATIONER, MUSIC AND PRINT SELLER,
PRINTER, BOOKBINDER, &c.

Fancy Stationery.--Bibles, Prayers, and Church Services.--Periodical Publications.
PLAIN AND ORNAMENTAL PRINTING OF EVERY DESCRIPTION.

1853

July 1 - 5 yr Scrap Account Book *L. S. D.*
extra quality labelled - - 10.0

Paid H Matthews
April 20th 1853

1850	The Feoffees of the Chamber of Colyton		
	To W. Power <i>D^{us}</i>	<i>L. S. D.</i>	
	To a piece of Elm Timber	"	9.0
	To work done at Hovington as per Contract	H. 10	0
	To six new weather boards fixed on brackets &c to front doors at Hovington	"	14.0
		<u>H. 24</u>	<u>0</u>

Settled Feb^r 11th 1853
Daniel Power

Colyton Jan. 1, 1853

L.S. 2/6 Rec^d from Mr. Higgins the sum of eight pounds two shillings and six pence, being a Quarters salary for the Boys on the foundation of the Feoffee Parish School of Colyton due Dec^r 25, 1852

Perfoc. W. Skinner *J. M. Stirling*

1852 *Mr Stodge*
to J Periman

Oct 1	Mason & boy Repairing	2
	Kill of Fowhey	4.0
	one Barrow of Mortar and Slates	1.6
Nov 7	Mason and boy	3
	Repairing Chimney	6.0
	Mortar Slates & 18 Bricks	3.9
		<u>15.3</u>

Dec 1 Paid J Periman


1852

Mr^r Poster Dr to
John Loveridge

Nov^r 19th

1/2 Days work repairing floor	1	4
14 ^{ft} of Elm board at 2 1/2 per foot & 1/2 100 of 6 Nails	3	2
29 th 1/2 Day repairing basement & Floors	1	4
Hinge Screws board & Nails	1	"
1 Day 2 hours to repairs & Steeping Stairs	3	2
3 ^{ft} inch Deal at 2 1/2. 22 ^{ft} 1/2 in at 1 1/2 per foot	3	4
Door Hinge & 1/2 100. 6 Nails		10 1/2
	<hr/>	
	£	11 2 1/2

Settled March 12
John Loveridge

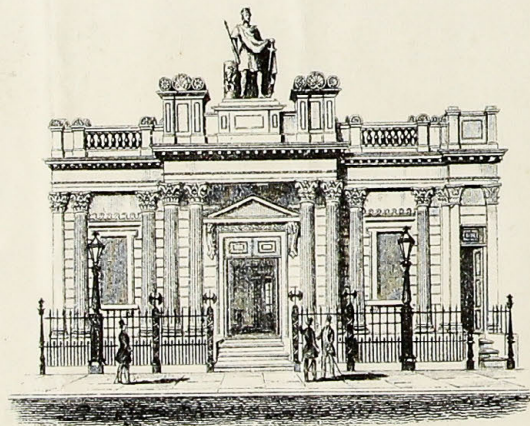

WEST OF ENGLAND
FIRE AND LIFE INSURANCE OFFICE,
EXETER.

Office in London, 20, Bridge Street, Blackfriars.

Colyton March 26th 1853

FIRE POLICY N^o. 189059
SUM INSURED £ 470
Premium £ 12 3
Duty £ 14 1
£ 16 4

Received of Mr. The Treasurers of Colyton

the Sums mentioned in the Margin, for the Renewal of the
said Policy from LADY-DAY 1853 to LADY-DAY 1854

J^{no} Drouce Son. Agent.

N.B. Life Insurances effected at Reduced Premiums, and the Insured participate in the Surplus every 5th Year.

1862

W^m Higgings Dr to
John Loversidge

Oct 15	34 Days work at Miss Spurways rep Stute Floor Skirting and Window	1	0
	5 Feet of inch by 9 deal 6 to 34	2	
	$\frac{1}{2}$ 100 6 Blaps $\frac{1}{2}$ Paint 3	1	4
	28 $\frac{3}{4}$ by 4 Oak		6
Nov ^r 15	50 $\frac{1}{2}$ of Deal ^{work} in Vineys back House	5	
22	Labour Timber nails at Vineys door &c	1	3
Decr 11	1 day and $\frac{1}{4}$ to Vineys & Mondays	3	4
	8 $\frac{1}{2}$ 3 $\frac{1}{4}$ by 9 Deal, 5 $\frac{1}{2}$ of inch do for Stakes & Nails	2	0
	3 $\frac{1}{2}$ of inch by 9 deal $\frac{1}{2}$ 100 Nails		9
30	Ship board at Spears door		8
		17	7

Carried over

		£	s	d
	Brought over		19	9
Janry 12 th	Labour & Materials to Vineys door		1	3
26	Repairs to the lower Cottage Oak sill to front door 7 ft of 2 by 3 fir labour and nails to the stairs		3	2
March 28	1/2 day Rep door to Vines house		1	4
	7 ft of 1/2 ⁱⁿ deal 10 ft 2 ft 3 by 4 Oak 100 of 4 ⁱⁿ clasp		1	8 1/2
30	At Miss Spurway 11 ft 3/4 red deal 9 ⁱⁿ wide at 2			
	11 ft 0 ⁱⁿ 7 ⁱⁿ wide at 1 1/2 per foot		3	2 1/2
	3/4 day work Rep Office floor garden house floor and washing benches nails &c		2	4
		£	1	10 7

Settled April 9th
L. Beveridge

Mrs Beveridge

1852

Horiton

Oct 2

Feoffees of Colyton

to Peter Brown

for Making and painting

two Chimney Boards of

5^{or} 12 pd Peter Brown

1859

The Treasurers of Colyton

To J & S Smith Plumbers
L & D

To oak used by J Pavey for Piers
of Hurdles

2 5

1860

June 1st 4 ft 3 inches of Pipe to Upper
Conduit

6 8

2 1/2 lb Solder to do

2 5

Two Leathers to Pumps in kitchen

2 5

Nov 13th

14 1/2 lb Mittell L^d to front of Shop
at Hamilton

2 2 10 1/2

11 1/2 ft pipe for waste water 1/2

13 5

5 lb Solder to do

5

Well and pipe Hooks to do

3

14 One Day for self & Man

5 6

1/2 Day & finishing do

3 3

1 New Stout glass for
Man light

3 5

Oct 8 1 Pane in Lamp at Colyton

1 2

Nov 23 4 Panes in Pewee Room

1 8

Repairing pipe & Strainer
in Mr Whites Yard


2 5

Or by 137 lb Old Lead at 2

4 18 0 1/2

1 2 10

£ 3 15 2 1/2



1/59
 Messrs Trill to
 Mr Goleman on the
 for work done
 for time & order
 within side & labour
 within the front
 of the House
 Settled 3.00
 To Goleman 3.00
 6

No. 464 to 473 HONITON UNION.
 PARISH OF HONITON, the 6 day of Oct 1859.
 Received of Mr. Colyton Feoffees
 the sum of fifteen shillings 10/2 in respect of the
 Poor Rate of the above Parish, viz. —
 Rate made the 15th day of August, 1859, on
 £ 31-15 Assessment, at 1s. in the Pound. 15 10 2
 Arrear of former Rate

No. 483 to 492 HONITON UNION.
 PARISH OF HONITON, the 17 day of June 1859.
 Received of Mr. Colyton Feoffees
 the sum of fifteen shillings 10/2 in respect of the Poor Rate
 of the above Parish, viz. —
 Rate made the 20th day of April 1859. on £ 31-15
 Assessment, at 1s. in the Pound 15 10 2
 Arrear of former Rate
 TOTAL
 G. Coatesford Assistant Overseer.

143
 Olney 5th May 1859
 Mr. W. Blouge
 To Samuel Mearns Dr
 Deb't Monday taking off locks & fixing " 2 8
 Tues Monday getting up shutter & " 3 6
 10/10 sup. 1 inch Elm 3/4. Oak 3/4. Nail 3/4 " 3 6
 1861 Apt. 2 Paid. H. Schmidt " 9 8 1/2

Feoffees of Colyton to
 1859 D. Ware Dr
 100 Bags Potatoes } 13 5 10
 at 2/5 a bush }
 Settled March 23rd 1859
 The [Signature]
 [Stamp: RECEIPT FOR PAID TO THE FEOFFES OF COLYTON]
